



Andy Wilke
Phone: (920)659-1487

Colt Chauvin
Phone: (920) 460-5054

PROJECT UPDATE – Weekly Update

Subject: Project Update

Date: 4/29/21

Project Report – Periodic Progress Summary

Key accomplishments this week:

- Electrical in wall rough-ins complete in the classroom wing.
- HVAC ductwork 95% hung throughout the project.
- Plumbing in wall rough-ins complete throughout the entire project.
- 100% of wood blocking installed.
- Sheetrock install has begun in the classroom wing.
- Underground power main installed to the transformer pad.
- Sprinkler piping 100% installed.
- All windows installed.

Upcoming tasks next week:

- Insulate interior walls.
- Complete sheet rock install in the classroom wing and begin in the kitchen area.
- Continue working on MEP rough-ins.
- Paint structural steel and ductwork in the gymnasium.
- Install transformer and CT cabinet on transformer pad.
- Set mechanical equipment in the mezzanine area.
- Pressure test sprinkler lines.

This week's weather:


Time	Temperature (° F)			Wind Speed (mph)			Precipitation (in)
Apr	Max	Avg	Min	Max	Avg	Min	Total
25	40	36	34	21	15	9	0.00
26	52	41	34	15	6	0	0.01
27	65	49	35	12	3	0	0.00
28	70	51	35	23	10	3	0.00
29	62	39	27	26	11	3	0.00



All windows installed.



Sprinkler pipes and ductwork installed in the gymnasium.

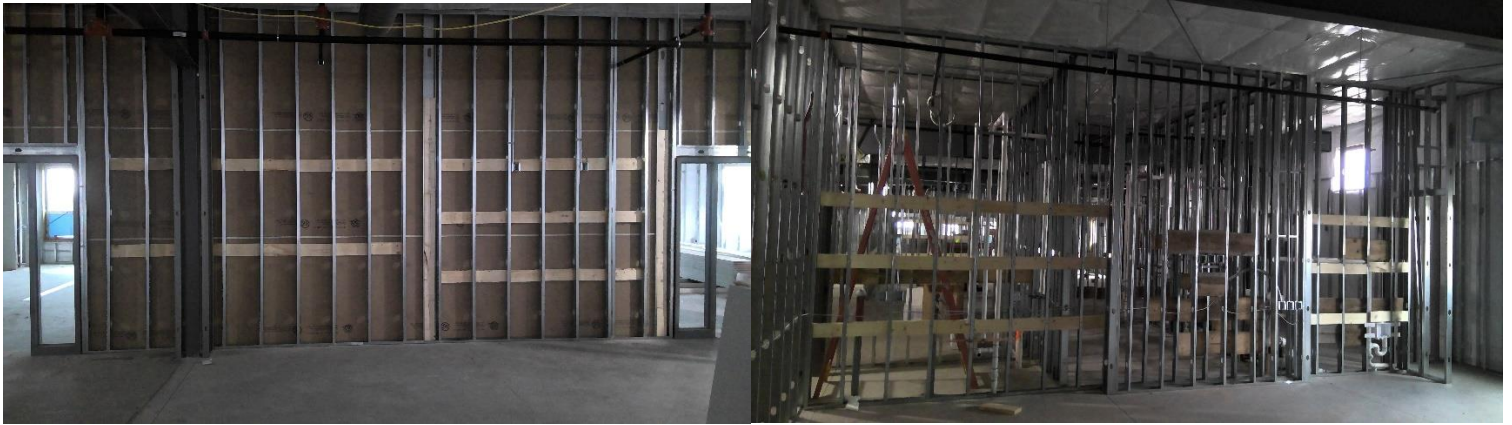

All wood blocking complete throughout the project.



Started hanging sheet rock in the classrooms.

